| Fin Project ID Number 1 | Project Description | Letting Date | Start Date | Early Finish | Projected Completion | Procur. Time | Contract Duration | Contract Dur Est'd? | Projects $$ | Contract Amt Est'd? |
|---|---|---|---|---|---|---|---|---|---|---|
| **HEFT** | | | | | | | | | | |
| ROJAS | | | | | | | | | | |
| 4159051 52 | Okeechobee ML Express Lanes/NW 74 St I/C (MP 32) | | 22JAN07A | 14MAR10 | 14MAR10 | 0 | 990 | | 65,594,827 | |
| 4232001 52 | Resurface HEFT MP 12-17 & 20-23 | 15JUL08 | 17JAN09A | 30NOV09 | 30NOV09 | 90 | 305 | | 5,550,244 | |
| 4195781 52 | Resurf/Safety Improvs HEFT Miami-Dade Co MP 0-9 | 22AUG08 | 18FEB09A | 11JUN10 | 11JUN10 | 90 | 480 | | 8,988,742 | |
| 4175441 52 | HEFT Conversion AET.PHASE-1 & PHASE-2 | 21MAY09 | 14SEP09A | 27SEP11 | 27SEP11 | 0 | 743 | | 33,019,060 | |
| 4175471 52 | HEFT Conversion To All Elect. PHASE 3 | 21MAY09 | 30SEP09A | 07SEP11 | 07SEP11 | 0 | 707 | | 24,795,000 | |
| 4196021 52 | Resurf/Safety Improv's HEFT Broward Co. MP 39-44 | 13OCT09 | 04JAN10* | 15APR10 | 01APR10 | 0 | 102 | | 2,688,415 | YES |
| 4261551 52 | Resurf HEFT MP-9.2/9.8 MP16.8/20.4 (NOT ADOPTED) | | 05JUL10* | 07SEP11 | | 0 | 430 | YES | 7,100,000 | YES |
| 4159053 | Landscaping Okeechobee toll Plaza (MP32) | | 01OCT10* | 08JAN11 | 08JAN11 | 0 | 100 | YES | 777,038 | YES |
| 4154622 52 | HEFT AET PHASE-4 | 08APR11 | 08JUL11* | 16JUN13 | 16JUN13 | 0 | 710 | YES | 17,913,700 | YES |
| 4154871 52 | HEFT SIGNAL IMPROVEMENT @ SW211TH ST. | 12JUL11 | 05FEB12* | 06JUN12 | 06JUN12 | 0 | 123 | YES | 351,690 | YES |
| 4060961 52 | HEFT-From N.of Eureka To Kendall Dr (PKG-B) | 10JUL18 | 11OCT18* | 23OCT23 | 23OCT23 | 0 | 1,839 | YES | 229,017,800 | YES |
| 4150511 52 | Widen HEFT From Kendall DR. to 60th St. Canal Br | 13JUL21 | 21OCT21* | 02APR25 | 02APR25 | 0 | 1,260 | YES | 114,439,955 | YES |
| 4150514 52 | Widen HEFT From 60th St. Canal Br.to SR-836 | 13JUL21 | 21NOV21* | 03MAY25 | 03MAY25 | 0 | 1,260 | YES | 208,588,000 | YES |
| 4154881 52 | HEFT-mainline Mill Dr(SW216)TO Eureka Dr.(PKG-A) | 13JUL21 | 22NOV21* | 17MAR25 | 17MAR25 | 0 | 1,212 | YES | 68,443,865 | YES |
| **SOUTHERN MAINLINE** | | | | | | | | | | |
| CASTILLO | | | | | | | | | | |
| 4060941 52 | Widen-Griffin Rd to N of Sunrise Blvd (MP 54-59) | 13JUN05 | 06FEB06A | 08SEP10 | 08SEP10 | 0 | 1,622 | | 96,085,954 | |
| 4060971 52 | Widen-N of Sunrise Blvd toAtlantic Blvd(MP 59-66 | | 06FEB06A | 29JAN10 | 21FEB10 | 0 | 1,400 | | 105,543,474 | |
| 4232011 52 | Resurf (Thin) Broward Co. MP 47-50 | 14APR09 | 19JUN09A | 14NOV09 | 14NOV09 | 60 | 45 | | 1,122,266 | |
| 4060944 52 | Widen NBnd-Peters Rd to N of Sunrise (MP 54-59) | 12MAY09 | 01NOV09* | 21MAR11 | 21MAR11 | 90 | 506 | | 29,768,500 | |
| 4060958 52 | Mill & Resrf. HEFT TO GRIFFIN RD. | 13JUL10 | 11OCT10* | 05MAR12 | 05MAR12 | 0 | 500 | YES | 5,523,861 | YES |
| 4060974 52 | Widen N Bnd-N of Sunrise to Atlantic (MP 59-66) | 09FEB10 | 27OCT10* | 05NOV12 | 05NOV12 | 150 | 741 | | 46,985,800 | |
| 4061505 52 | Mill & Resrf. Atlantic To Sawgrass | 13SEP11 | 12DEC11* | 20MAY13 | 20MAY13 | 0 | 526 | YES | 5,613,685 | YES |
| 4060954 52 | Widen-N of Johnson St to Griffin Rd (MP 50-53) | 12JUL16 | 12OCT16* | 29MAR20 | 29MAR20 | 0 | 1,230 | | 63,570,000 | YES |
| 4061501 52 | Widen-Atlantic to N of Sawgrass Expwy (MP 66-71) | 10JUL17 | 09OCT17* | 30MAY22 | 30MAY22 | 0 | 1,695 | | 124,117,000 | YES |
| 4061031 52 | Sunrise Blvd.Interchange Modification (MP 58) | 10JUL18 | 18OCT18* | 08JUN20 | 08JUN20 | 0 | 600 | YES | 66,248,610 | YES |
| 4060951 52 | Widen-HEFT to N Johnson w/Hollywood I/C(MP 47-50 | 09JUL19 | 12OCT20* | 27FEB25 | 27FEB21 | 0 | 1,600 | YES | 40,707,380 | YES |
| RUSH | | | | | | | | | | |
| 4241551 52 | Reconstruct Jupiter Tandem Trk Stage Lot (MP 116 | 10FEB09 | 19MAY09A | 19SEP09A | 19SEP09 | 0 | 90 | | 374,436 | |
| 4222771 52 | Rsrf/Reconstruct NB Exit Ramp@Ft Pierce (MP 152) | 10FEB09 | 09JUN09A | 25FEB10 | 12FEB10 | 60 | 250 | | 1,272,748 | |
| 4207351 52 | St. Lucie Interchange Improvements (MP 142) | 10MAR09 | 02JUL09A | 25FEB10 | 25FEB10 | 60 | 236 | | 1,534,048 | |
| 4217201 52 | Resurf/Safety Impr Indian River Co MP 173 to 178 | 12MAY09 | 17JUL09A | 21DEC09 | 21DEC09 | 0 | 150 | | 3,689,970 | |
| 417544 352 | Bridge Painting @ Miami Gardens | 16JUN09 | 01AUG09A | 17JAN10 | 13NOV09 | 40 | 140 | | 1,244,357 | |
| 4061444 52 | Lake Worth Interchange Modification | 21APR09 | 11AUG09A | 03JUN11 | 03JUN11 | 0 | 681 | | 17,434,969 | |
| 4196031 52 | Resurf/Safety Improv's St Lucie Co MP 169 to 173 | 11AUG09 | 15OCT09A | 14DEC09 | 14DEC09 | 0 | 64 | | 1,869,990 | |
| 4193291 52 | Canal Protection in Martin Co. | 14JUL09 | 16OCT09A | 13FEB10 | 13FEB10 | 0 | 121 | | 1,780,469 | |
| 1907741 52 | Boca Toll Data Center Parkg. lot | | 20NOV09* | 18MAY10 | 18MAY10 | 0 | 180 | YES | 1,393,349 | YES |
| 417544-352 | Noise Wall @ Miami Gardens | 09JUN09 | 14DEC09* | 31JAN10 | 31JAN10 | 157 | 49 | | 1,515,295 | |
| 4232041 52 | Resurf Mainline Spur Miami-Dade Co. MP 0 to 3.3 | 13JUL10 | 13OCT10* | 30APR11 | 30APR11 | 60 | 200 | YES | 4,040,668 | YES |
| 4193311 52 | Canal Protection in Indian River Co. | 13JUL10 | 29NOV10* | 27MAY11 | 27MAY11 | 60 | 180 | YES | 2,271,880 | YES |
| 4193281 52 | Canal Protection in Okeechobee Co. | 15JUL14 | 01DEC14* | 29MAY15 | 29MAY15 | 60 | 180 | YES | 2,084,000 | YES |

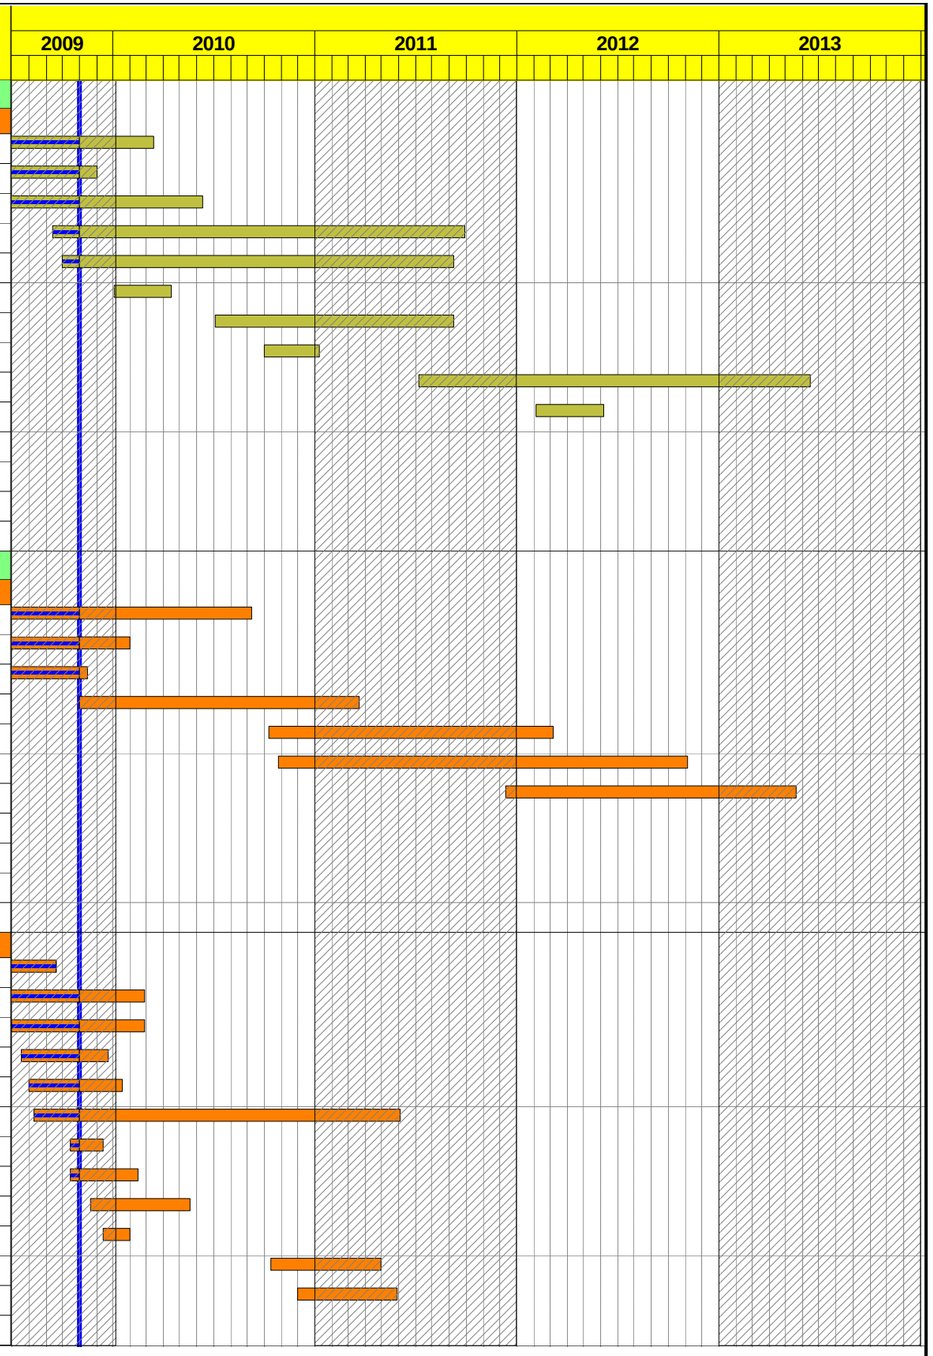


© Primavera Systems, Inc.

**FLORIDA'S TURNPIKE ENTERPRISE**
**CONSTRUCTION DIVISION**

**SUMMARY SCHEDULE**
**ACTIVE AND PLANNED PROJECT AS OF 11/1/09**

PB 100 YEARS

| Fin Project ID Number 1 | Project Description | Letting Date | Start Date | Early Finish | Projected Completion | Procur. Time | Contract Duration | Contract Dur Est'd? | Projects $$ | Contract Amt Est'd? |
|---|---|---|---|---|---|---|---|---|---|---|
| 4223491 52 | Replace Ramp Bridge at PGA Blvd (MP 109) | 10JUL18 | 08OCT18* | 21DEC19 | 21DEC19 | 0 | 440 | YES | 9,848,030 | YES |
| 4223501 52 | Replace Ramp Bridge at Jupiter (MP 116) | 10JUL18 | 10OCT18* | 24OCT19 | 03NOV19 | 0 | 380 | YES | 11,669,305 | YES |
| 4061441 52 | Widen-N Boynton to Lake Worth Rd & I/C(MP 86-93) | 15JUL20 | 22OCT20* | 09MAR25 | 09MAR25 | 0 | 1,600 | YES | 101,360,995 | YES |
| 4061431 52 | Widen-Lake Worth Rd to Okeechobee Blvd (MP 93-99 | 12JUL22 | 19OCT22* | 25AUG24 | 25AUG24 | 0 | 677 | YES | 79,357,530 | YES |
| HUDSON | | | | | | | | | | |
| 4171281 52 | Pompano Operations Center Expansion (MP 65) | | 02JUN08A | 15DEC09 | 15DEC09 | 0 | 390 | | 8,536,679 | |
| **NORTHERN MAINLINE** | | | | | | | | | | |
| GOMEZ | | | | | | | | | | |
| 4195701 52 | Resurf/Safety Improv's Orange Co. MP 249 to 255 | 09DEC08 | 06MAY09A | 08SEP09A | 08SEP09 | 0 | 105 | | 4,146,748 | |
| 4193301 52 | Canal Protection in Lake Co. | 17JUL12 | 03DEC12* | 06APR13 | 06APR13 | 60 | 125 | YES | 4,182,000 | YES |
| 4193251 52 | Canal Protection in Sumter Co. | 16JUL13 | 02DEC13* | 11MAR14 | 11MAR14 | 60 | 100 | YES | 1,668,000 | YES |
| CHINELLY | | | | | | | | | | |
| 4061481 52 | Widen Mainline-I-4 to N of Gotha Rd (MP 259-265) | | 16JUL07A | 28SEP10 | 28SEP10 | 0 | 1,130 | | 93,169,425 | |
| 4061483 52 | Widen Mainline-Hemple to N of Beulah(MP 266-269) | | 04FEB08A | 26AUG10 | 26AUG10 | 0 | 900 | | 53,544,580 | |
| 4061461 52 | Widen Mainline-Beulah Rd to S.R. 50 (MP 269-274) | 18SEP08 | 07JAN09A | 30MAY12 | 30MAY12 | 0 | 1,242 | | 77,939,455 | |
| 4193261 52 | Canal Protection in Osceola Co. | 19JUL11 | 28NOV11* | 18AUG12 | 18AUG12 | 60 | 265 | YES | 9,461,000 | YES |
| 4231981 52 | Resurface Lake Co. SB Only MP 282 to 298 | 13DEC11 | 14MAY12* | 08JAN13 | 08JAN13 | 60 | 240 | YES | 22,476,044 | YES |
| 4193271 52 | Canal Protection in Orange Co. | 21JUL15 | 30NOV15* | 27MAY16 | 05MAR16 | 60 | 180 | YES | 1,560,000 | YES |
| **MARTIN ANDERSEN BEACHLINE EXPRESSWAY** | | | | | | | | | | |
| GOMEZ | | | | | | | | | | |
| 4223301 52 | Widen Beachline-Tpk to Sand Lake Rd (MP 4-6&7-8) | | 26MAY08A | 14APR11 | 14MAR11 | 0 | 1,035 | | 48,830,890 | |
| **SOUTHERN CONNECTOR EXTENSION** | | | | | | | | | | |
| CHINELLY | | | | | | | | | | |
| 4213091 52 | Paint Multiple Bridges @ Southern Conn Extension | 13JUL10 | 13JAN11* | 11JUN11 | 11JUN11 | 90 | 150 | YES | 749,028 | YES |
| 4232021 52 | Resurface Southern Connector Extension MP 1 to 6 | 14DEC10 | 16MAY11* | 08JUL12 | 08JUL12 | 60 | 420 | YES | 3,878,198 | YES |
| **SEMINOLE I EXPRESSWAY** | | | | | | | | | | |
| GOMEZ | | | | | | | | | | |
| 4175452 52 | Lake Jesup Plz Express Lanes/Rsrf Sem Exwy 46-50 | 17JUN08 | 03NOV08A | 21APR11 | 21APR11 | 0 | 900 | | 30,747,400 | |
| 4175451 52 | Widen Seminole Expwy-Univ Dr to SR 434 (Des/Bld) | 09JUL19 | 17OCT19* | 28JAN23 | 28JAN23 | 0 | 1,200 | YES | 88,028,935 | YES |
| **POLK PARKWAY** | | | | | | | | | | |
| GOMEZ | | | | | | | | | | |
| 4165371 52 | Widen Polk Pkwy & Pace Rd I/C MP 18-24(Dsgn/Bld) | 30JUL09 | 17DEC09* | 16NOV11 | 16NOV11 | 0 | 700 | | 27,832,600 | |
| 4231991 52 | Resurface Polk Pkwy MP 8 to 17 | 13DEC11 | 13MAY12* | 04SEP13 | 08MAR13 | 60 | 480 | YES | 34,361,721 | YES |
| **VETERAN'S EXPRESSWAY** | | | | | | | | | | |
| GOMEZ | | | | | | | | | | |
| 4061511 52 | Widen Vet's-Memorial Hwy-N of Anderson ML(MP 1-6 | 10JUL18 | 20OCT18* | 23SEP23 | 23SEP23 | 0 | 1,800 | YES | 243,659,265 | YES |
| **SUNCOAST PARKWAY I** | | | | | | | | | | |
| GOMEZ | | | | | | | | | | |
| 2589451 52 | Lutz-Lake Fern Rd I/C Incl Toll Plazas (Des/Bld) | | 10OCT08A | 29MAR10 | 26FEB10 | 0 | 400 | | 14,744,669 | |
| **SUNCOAST PARKWAY II** | | | | | | | | | | |
| CHINELLY | | | | | | | | | | |
| 4052701 01 | Suncoast Parkwayy II Section - 1 | 09JUL19 | 14OCT19* | 11OCT27 | 11OCT27 | 0 | 2,920 | YES | 447,004,370 | YES |
| 4052701 04 | Suncoast Parkwayy II Section - 2 | 09JUL19 | 14OCT19* | 11OCT27 | 11OCT27 | 0 | 2,920 | YES | 447,004,370 | YES |
| 4052701 05 | Suncoast Parkwayy II Section - 3 | 09JUL19 | 14OCT19* | 11OCT27 | 11OCT27 | 0 | 2,920 | YES | 447,004,370 | YES |

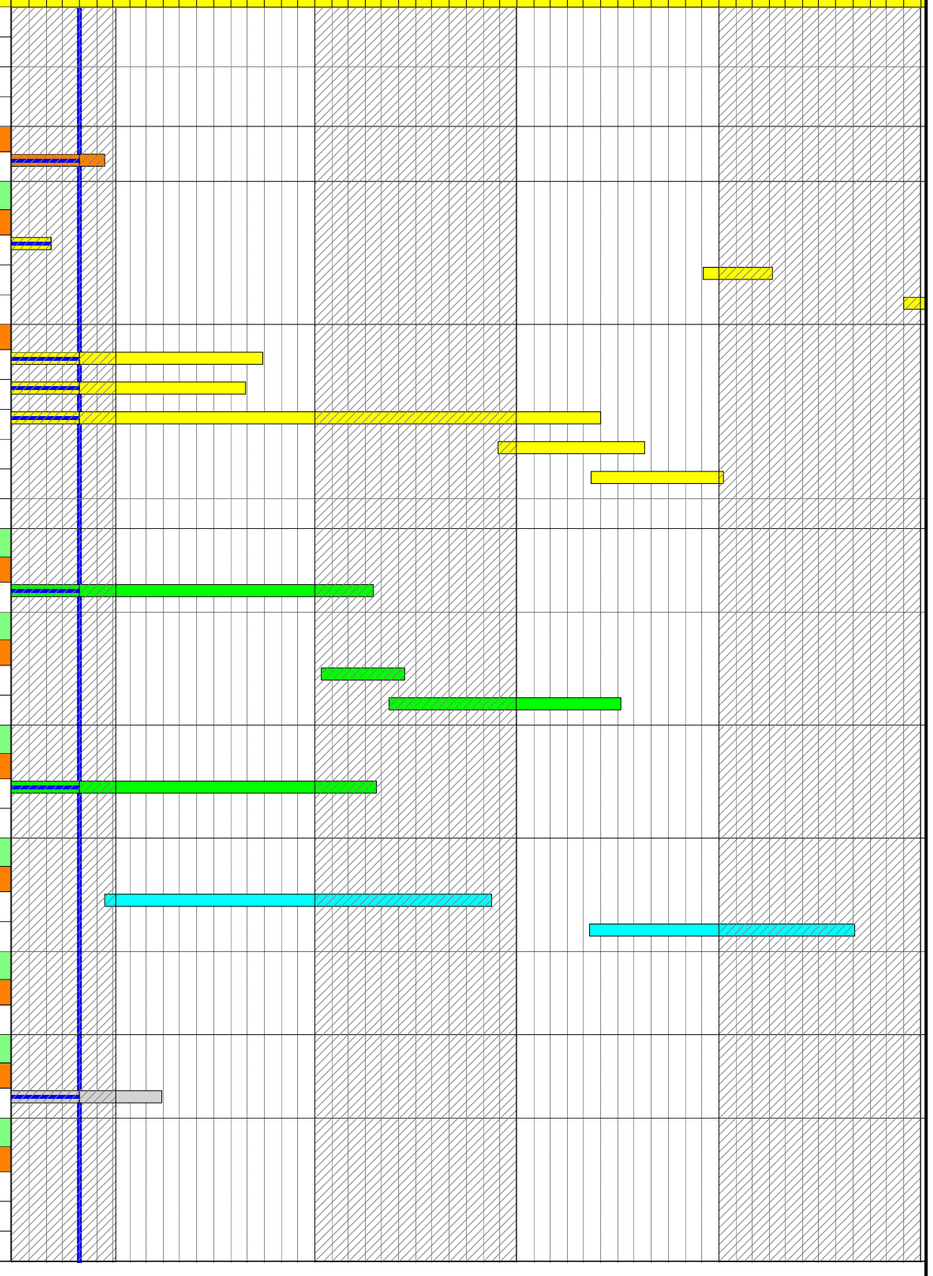


© Primavera Systems, Inc.

**FLORIDA'S TURNPIKE ENTERPRISE**
**CONSTRUCTION DIVISION**

**SUMMARY SCHEDULE**
**ACTIVE AND PLANNED PROJECT AS OF 11/1/09**
